

CREATE PROGRAM SCHEDULE

Activity Name	Duration % Complete	Start	Finish	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015	2016	2017	2018	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036		
CREATE Program	70.66%	15-Aug-05 A	13-Feb-29																																	
Western Avenue Corridor	70.66%	15-Aug-05 A	13-Feb-29																																	
WA1 - Ogden Jct. Improvements	70.66%	15-Aug-05 A	13-Feb-29																																	
PRELIMINARY DESIGN AND ENVIRONMENTAL STUDIES (PHASE I)	100%	15-Aug-05 A	22-Nov-10 A																																	
RDG Constructability Review and Approval	100%	10-Jul-07 A	10-Jul-07 A																																	
Prepare Scope Packet For CREATE Approval Process	100%	15-Aug-05 A	16-Jul-07 A																																	
Primary Railroad Submittal To CTCO	100%		16-Jul-07 A																																	
CTCO Review and Approval	100%	16-Jul-07 A	16-Jul-07 A																																	
CTCO Approval	100%		16-Jul-07 A																																	
Develop Revised Western Ave Concept	100%	05-Dec-05 A	18-Jul-07 A																																	
CPG Scope Review and Approval (required)	100%		18-Jul-07 A																																	
CREATE Implementation Committee Scope Review and Approval (required)	100%		07-Sep-07 A																																	
CREATE Management Committee Scope Review and Approval	100%		01-Oct-07 A																																	
Develop IDOT State Rail Agreement - Design	100%	01-Jan-08 A	22-Jan-08 A																																	
Submit Initial Geometrics to IDOT	100%		22-Jan-08 A																																	
Environmental Class of Action Determination	100%	08-Aug-07 A	17-Aug-09 A																																	
Finalize Preliminary Design - 30% Plans and DA	100%	17-Aug-09 A	20-Aug-09 A																																	
Preliminary Engineering	100%	23-Aug-07 A	23-Jun-10 A																																	
IDOT Design Approval	100%	20-Aug-09 A	22-Nov-10 A																																	
DESIGN (PHASE II)	94.03%	15-Jun-10 A	08-May-23																																	
Draft Project Report	100%	17-Aug-10 A	22-Nov-10 A																																	
RFP For Bridge Design	100%	15-Jun-10 A	06-May-11 A																																	
IDOT State Rail Agreement - Design Approval	100%	01-Jun-11 A	06-Jul-11 A																																	
SRA for phase II design revision at IDOT	100%	30-Oct-14 A	15-May-15 A																																	
Structural Design RFP	100%	22-Jan-16 A	18-Apr-16 A																																	
Structural Design Consultant Negotiations	100%	19-Apr-16 A	30-Sep-16 A																																	
Obtain Construction Funding - Stage 1	100%	01-Jun-19 A	01-Aug-19 A																																	
Signal Final Design	100%	01-Dec-11 A	30-Oct-20 A																																	
IDOT Section 106 MOA	100%	18-Jun-19 A	01-Feb-21 A																																	
IDOT/SHPO Negotiate/Partners Sign MOA	100%		02-Feb-21 A																																	
Procure Right of Way	100%	01-May-20 A	06-May-21 A																																	
Prepare and Submit Plan, Specification & Estimates and IDOT State Rail Agreement Request - Procurement/Construction	100%	01-May-20 A	01-Oct-21 A																																	
Track Final Design	100%	01-Dec-11 A	30-Dec-21 A																																	
Structural Final Design	100%	04-Jul-16 A	30-Dec-21 A																																	
IDOT Tech Memo #3	100%	03-Jun-19 A	31-Dec-21 A																																	
Cultural Review of ESR-F	100%	01-Sep-21 A	28-Feb-22 A																																	
Railroad Prepares for Budget Review	50%	01-May-20 A	13-May-22																																	
IDOT/FHWA Plan, Specification & Estimate and State Rail Agreement Review	75.56%	01-Oct-21 A	16-May-22																																	
IDOT/FHWA Plan Specification & Estimate Approval	0%		16-May-22																																	

- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone


CONFIDENTIAL DRAFT

Project Schedule

Data Date: 01-May-22
 Printed: 21-Apr-22 14:59
 Page 1 of 2



CREATE PROGRAM SCHEDULE

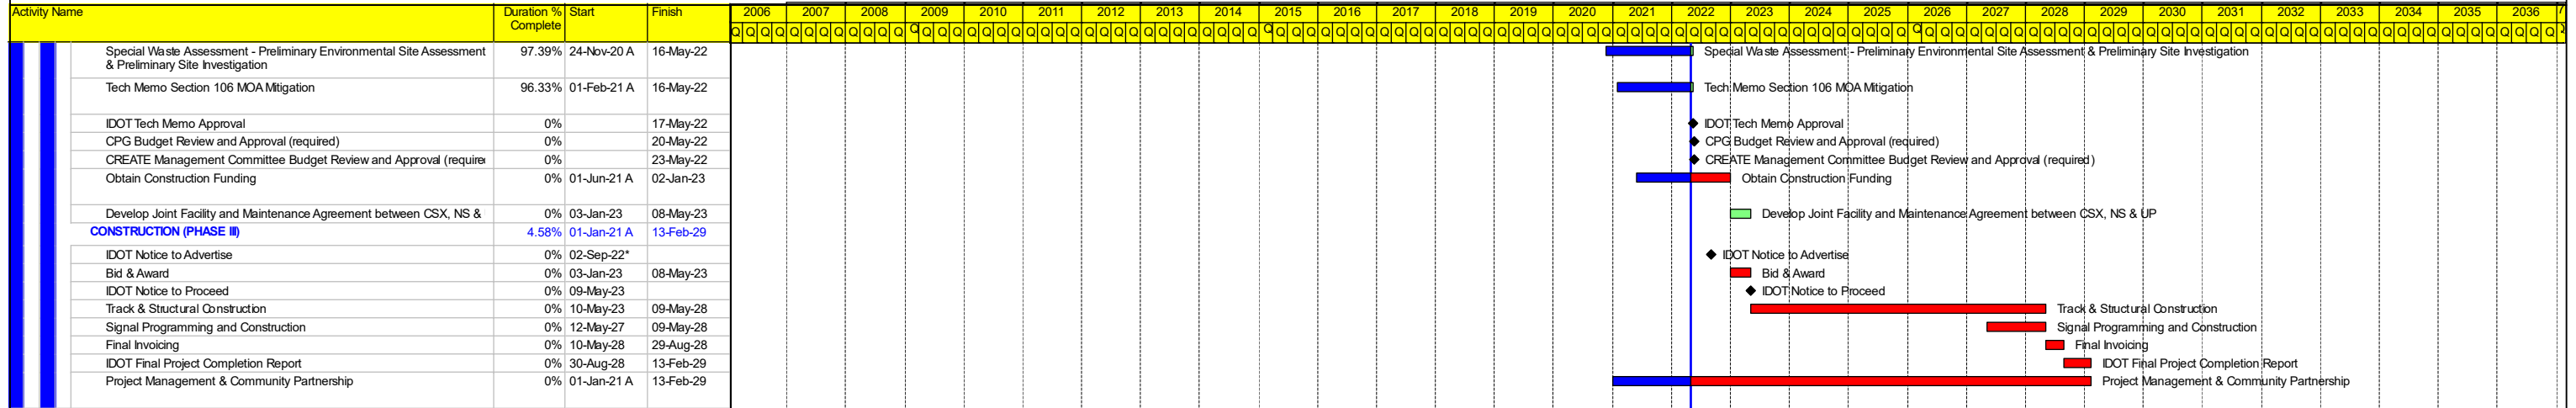

- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ Milestone

CONFIDENTIAL DRAFT

Project Schedule

Data Date: 01-May-22
Printed: 21-Apr-22 14:59
Page 2 of 2

