


Activity ID	Activity Name	At Completion Duration	Start	Finish	2020			2021			2022			2023			2024			2025			2026			2027			2028			2029			2030			2031			2032			2033		
					Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q			

<b>Public Involvement</b>		<b>2108</b>	<b>03-Dec-25 A</b>	<b>30-Dec-33</b>
<b>75th St. CIP Public Involvement Activities</b>		<b>2108</b>	<b>03-Dec-25 A</b>	<b>30-Dec-33</b>
INF0670	Union Outreach Event	0	03-Dec-25 A	03-Dec-25 A
INF0680	High School Engineering Competitions - Ongoing	2087	01-Jan-26*	30-Dec-33
INF1610	Grade School Bridge Building Events - Ongoing	2087	01-Jan-26*	30-Dec-33
INF1620	CAG Meetings - Ongoing	2066	30-Jan-26*	30-Dec-33
<b>Project P2</b>		<b>7618</b>	<b>20-Oct-04 A</b>	<b>30-Dec-33</b>
<b>75th CIP (P2) Preliminary Engineering and Environmental Studies (Phase I)</b>		<b>3394</b>	<b>20-Oct-04 A</b>	<b>24-Oct-17 A</b>
OS25610	75th CIP Environmental Impact Statement	2587	20-Oct-04 A	19-Sep-14 A
OS25660	FHWA Approves 75th CIP Final Environmental Impact Statement	0	19-Sep-14 A	19-Sep-14 A
OS25670	FHWA Approves 75th CIP Record of Decision	0	19-Sep-14 A	19-Sep-14 A
OS25750	FHWA Approves 75th CIP EIS Reevaluation	0	24-Oct-17 A	24-Oct-17 A
<b>P2 Design Environmental Activities</b>		<b>1651</b>	<b>01-Feb-21 A</b>	<b>31-May-27</b>
OS25370	P2 PESA Report - Draft	0	01-Feb-21 A	01-Feb-21 A
OS25390	IDOT/PMC/CMC Review P2 PESA Report - Draft	17	05-Mar-21 A	30-Mar-21 A
OS25440	P2 PSI Report - Draft 1	0	19-Mar-21 A	19-Mar-21 A
OS25410	P2 PESA Report - Final	0	30-Apr-21 A	30-Apr-21 A
OS25490	P2 PSI Report - Draft 2	0	30-Apr-21 A	30-Apr-21 A
OS25420	IDOT/PMC/CMC Review P2 PESA Report - Final	25	03-May-21 A	07-Jun-21 A
OS25450	IDOT/PMC/CMC Review P2 PSI Report - Final	25	03-May-21 A	07-Jun-21 A
OS25470	P2 PESA & PSI Comment Resolution	277	08-Jun-21 A	30-Jun-22 A
OS25510	Prepare P2 Special Waste Assessment (SWA)	45	02-Aug-21 A	04-Oct-21 A
OS25430	P2 PESA Complete	0	30-Jun-22 A	30-Jun-22 A
OS25480	P2 PSI Complete	0	30-Jun-22 A	30-Jun-22 A
OS25520	Complete P2 Special Waste Assessment (SWA)	0	30-Jun-22 A	30-Jun-22 A
OS25530	P2 - NEPA re-evaluation	261	01-Jun-26*	31-May-27
<b>P2 ROW</b>		<b>1515</b>	<b>09-Sep-21 A</b>	<b>30-Jun-27</b>
<b>P2 ROW Professional Services State Rail Agreement (SRA)</b>		<b>1321</b>	<b>09-Sep-21 A</b>	<b>01-Oct-26</b>
OS24770	RR submit selection process to IDOT	0	09-Sep-21 A	09-Sep-21 A
OS24780	IDOT review and approve selection process	5	01-Oct-21 A	07-Oct-21 A
OS24790	RR submits RFP scope to IDOT	5	08-Oct-21 A	14-Oct-21 A
OS24870	IDOT create SRA for signature	8	08-Oct-21 A	19-Oct-21 A
OS24800	IDOT assigns DBE goals	5	15-Oct-21 A	21-Oct-21 A
OS24880	RR sign SRA	1	21-Oct-21 A	21-Oct-21 A
OS24810	RR prepares revised scope and advertisement and submits to IDOT for approval	124	22-Oct-21 A	14-Apr-22 A
OS24890	IDOT sign SRA	1	03-Nov-21 A	03-Nov-21 A
OS24820	IDOT issues Notice to Advertise (NTA)	0	27-Apr-22 A	27-Apr-22 A
OS24830	RR submits advertisement to newspapers	1	28-Apr-22 A	28-Apr-22 A
OS24840	RR perform selection process including pre-bid meetings and send to IDOT	56	29-Apr-22 A	18-Jul-22 A
OS24850	IDOT review and approve selection	32	19-Jul-22 A	01-Sep-22 A
OS24860	FHWA review and approve selection	10	01-Sep-22 A	15-Sep-22 A
OS25500	Metra scope negotiations with consultant	49	03-Oct-22 A	09-Dec-22 A
OS25540	IDOT approval for funding increase	48	12-Dec-22 A	16-Feb-23 A
OS25550	Metra board approval for funding increase	20	17-Feb-23 A	17-Mar-23 A
OS24900	NTP issued	3	20-Mar-23 A	23-Mar-23 A



█ Remaining Level of Effort   
 █ Actual Work   
 █ Critical Remaining Work  
█ Actual Level of Effort   
 █ Remaining Work   
 ◆ Milestone

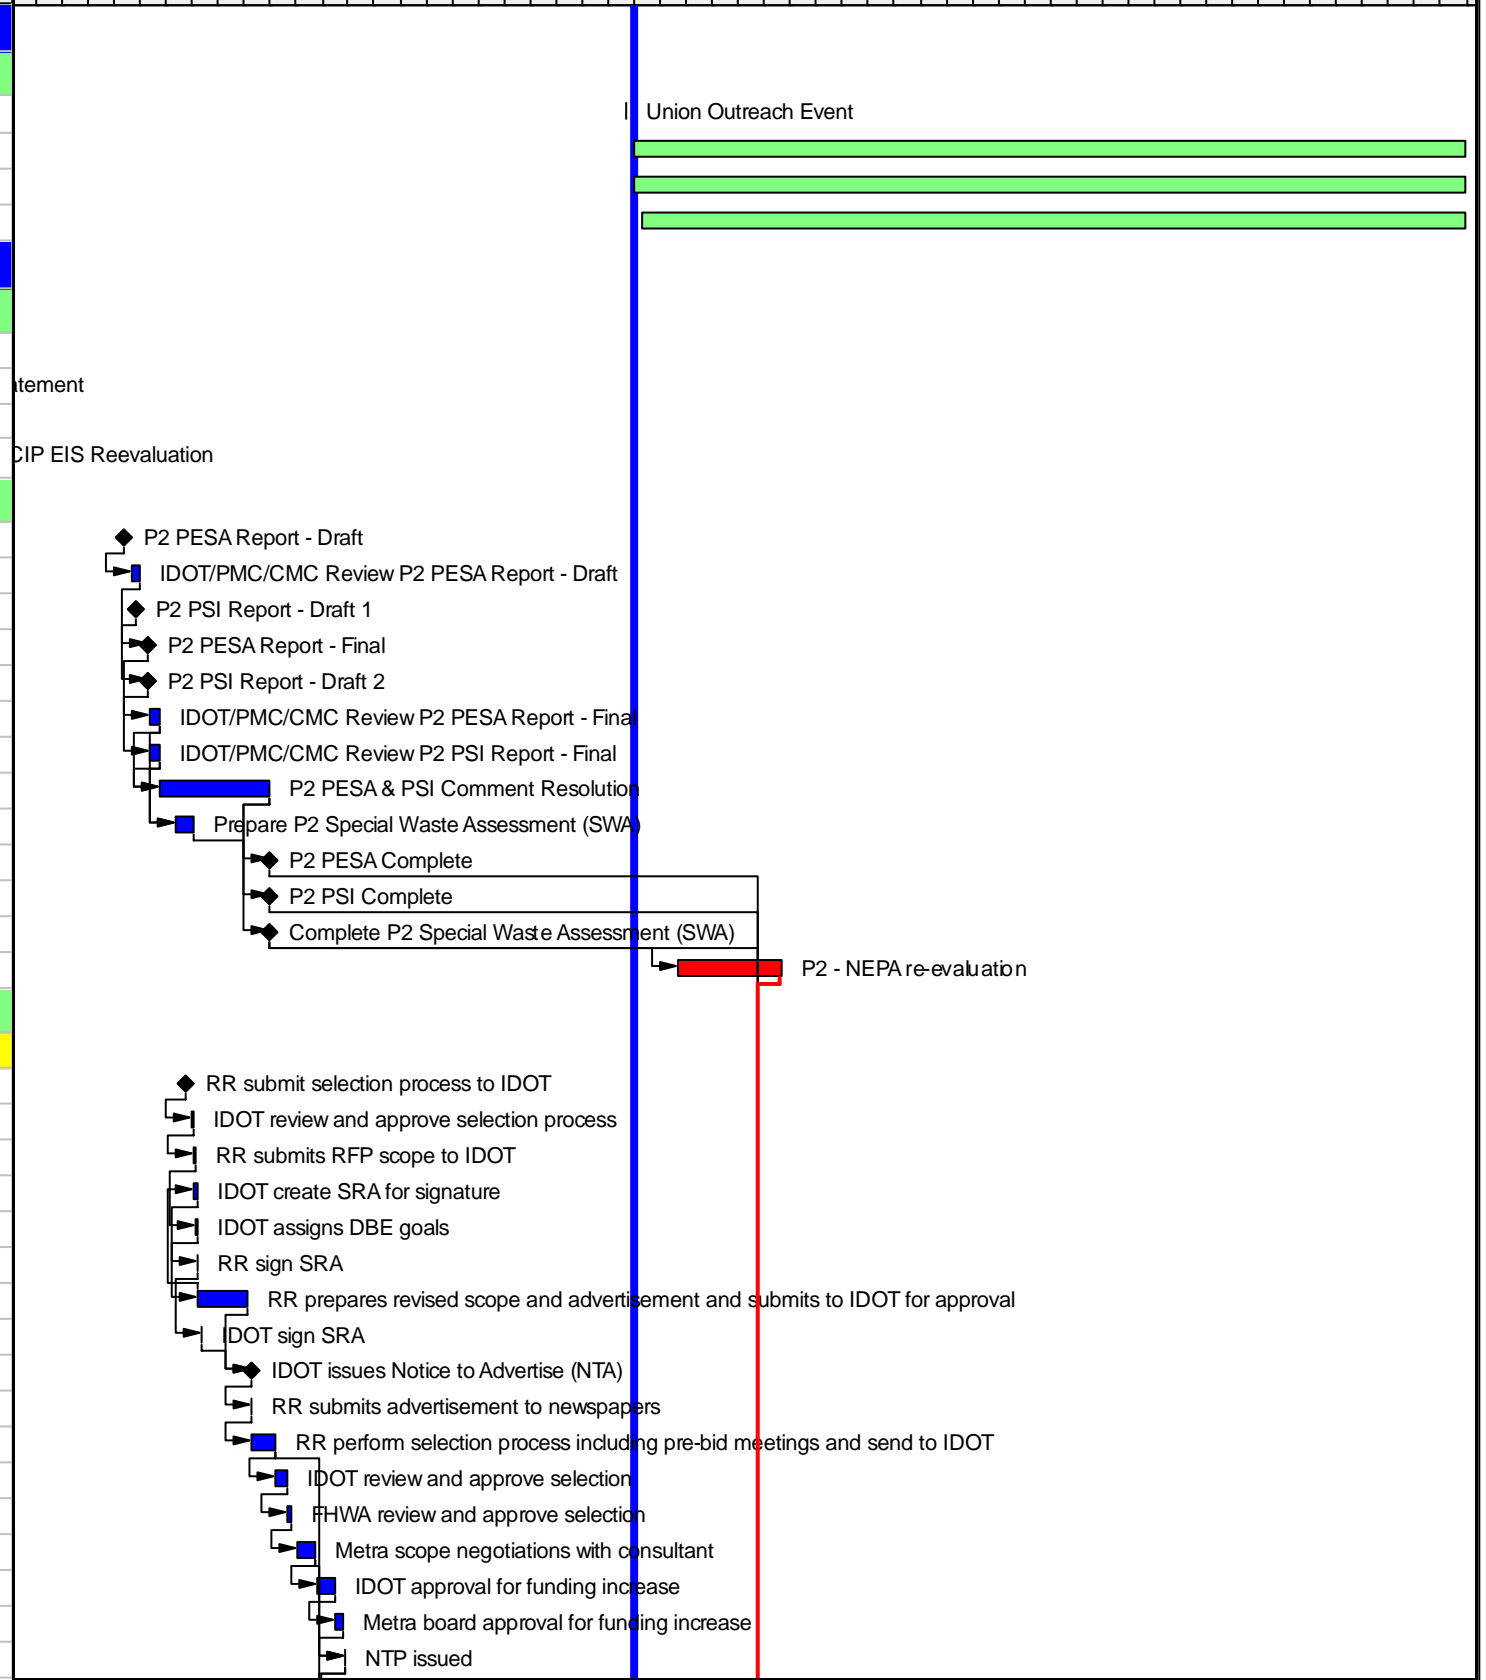



